

DEPARTMENTAL MONTHLY REPORT

FOR THE MONTH OF

April 2026

DEPARTMENTS REPRESENTED WITHIN THE REPORT:

Wastewater Operations (US Water)

Public Works

Engineering

Protective Inspections



WASTEWATER OPERATIONS (US Water)

MONTHLY REPORT

5/11/2026

Jenks Public Works Authority

City of Jenks
211 N. Elm Street
Jenks, Oklahoma 74037

Re: Monthly Operational Report for the Wastewater Treatment Plant, Lift Stations, and Booster Pump Stations

Dear JPWA:

In accordance with the requirements of our contract, we are pleased to provide the following monthly operational report by the second Tuesday of the following month to give an understanding of what has occurred at the Wastewater Treatment Plant (WWTP), Booster Pump Stations and Lift Stations. This report will also include regulatory reports; compliance reports, chemical usage, and any scheduled events that will be occurring in future months.

SUBMITTED TO: Robert Carr, Assistant City Manager
Barry Parsons, Public Works Director
Public Works Authority, City of Jenks
Aaron Voss, U.S. Water
Chris Gutschow, U.S. Water

We appreciate the opportunity to be of service to the City of Jenks and being your trusted partner in delivering essential water and wastewater services. We are available to discuss this report, or any other aspect of our operations, at your convenience.

Sincerely,

Rick Clark

Rick Clark, State Manager
(918) 649-4394
RClark@USWaterCorp.net

Rob Hulverson

Rob Hulverson, Project Manager
(918) 209-6492
RHulverson@USWaterCorp.net

Executive Summary

The Jenks Wastewater Treatment Facility is fully in compliance with discharge criteria established by the Oklahoma Department of Environmental Quality.

April was the first month of year four for the U.S. Water Utility Group at the Jenks Public Works Authority Wastewater Treatment Plant. We currently have five full-time employees. U.S. Water completed 180 work orders over the course of the month. Quarterly biomonitoring was conducted in the second week of April, with all results exceeding federal standards. There were three Sanitary Sewer Overflows in April, two at Kimberly Clark Lift Station due to a collapsed sewer line. And one at 106th and Elm Lift Station during a severe thunderstorm that may have caused an electrical surge.

Plant Maintenance Activities

- The UV channel at the plant was given its annual cleaning.
 - The Channel was turned off, banks removed.
 - Channel was drained, hosed out with a fire hose then bleached.
- Operators completed 180 preventative maintenance work orders.
- Aerator 1B on the oxidation ditch suffered a failure of the Lovejoy coupling that connects the motor to the aerator gearbox.
 - Plant staff had a new coupling sent overnight and replaced it within 48 hours.

Lift Station Maintenance Activities

Routine Maintenance

- De-ragging completed at:
 - Commerce Park
 - B Street
 - Frazier Meadows

Repairs & Equipment Upgrades

- Severe thunderstorms on April 4th caused numerous power outages and high wet well alarms at Oakwood and West Main lift Stations.
- Severe thunderstorms on April 14th caused numerous power outages on the north side of town and in the Yorktown Area. 5th and E St. lift station had multiple load sensors, a wet well board and their corresponding ports on the mission control board.
- An SSO occurred at 106th and Elm Lift Station during a severe thunderstorm, that may have caused an electrical surge. The battery, wet well board and old PLC system were all damaged as a result. A Vega level indicating radar was installed along with a backup float to prevent a future occurrence.


- A sink hole was discovered at Kimberly Clark Lift Station on the 13th. Flow totals from the lift station indicated significantly higher flows during heavy rainstorms. A collapsed line was suspected and turned over to Public Works personnel. During repairs, an enormous amount of dirt and gravel got into the lift station causing significant damage to both pumps that were installed at the time. Coordinated efforts between plant staff and the public works department resulted in the damaged pumps being pulled, the wet well of the lift station being vacuumed out and temporary pumps installed so that the public works personnel could replace the broken line from the manhole to the lift station.
- All thirty-two lift stations, and two booster stations were operational during the month of April. All thirty-four stations were inspected four times a week, wet well checks, checked pump operations and checked pumps in auto on Saturdays, Mondays, Wednesdays, and Fridays.

The following pages will provide an overview of the budget, operations, maintenance, and projects that have been completed for April 2026, for the Wastewater Treatment Plant (WWTP), Booster Pump Stations and Lift Stations in Jenks, Oklahoma

Year To Date Expense Cap Summary

Line Item	Cost To Date	Annual Budget	Remaining Balance	% Remaining
Chemicals WWTP	\$4,849.34	27,679.44	\$22,830.10	82%
Chemicals for Lift Stations & Water Booster Pump Stations	\$0.00	\$0.00	\$0.00	
Maintenance for WWTP	\$14,604.98	\$83,038.31	\$68,433.33	82%
Maintenance for Lift Stations & Water Booster Pump Stations	\$315.50	\$55,358.87	\$55,043.37	99%
Total	\$19,769.82	\$166,076.62	\$146,306.80	88%


Wastewater Treatment Plant Electric Usage

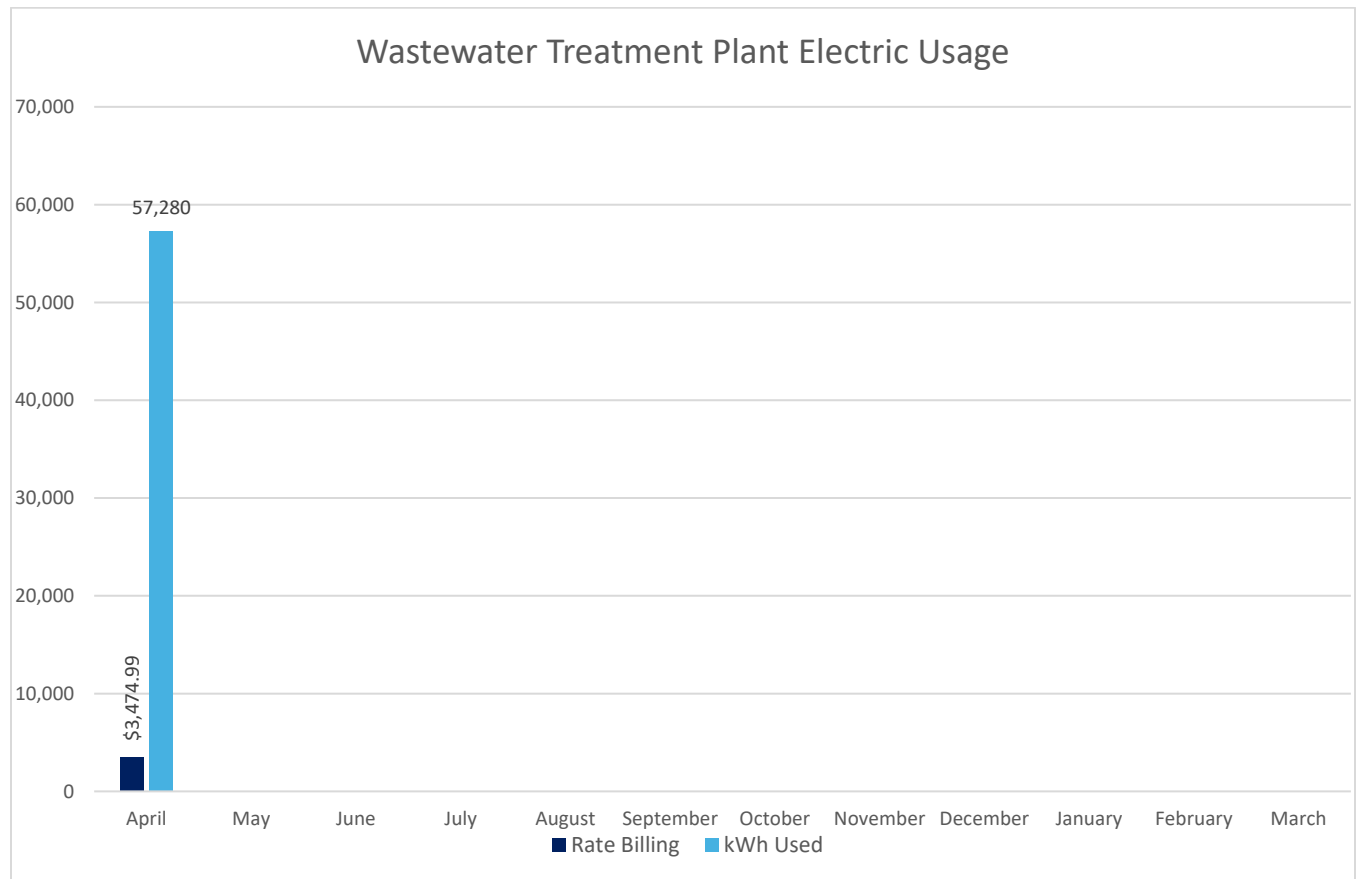



Key Performance Indicators (KPIs)


Parameter	Last	Min	Max	Avg
INF Total Flow (MG)	1.922	1.587	2.990	2.218
Effluent Flow Total (MG)	1.884	1.659	3.073	2.220
INF BOD5 (mg/L)	139	139	257	196
INF TSS (mg/L)	290	108	433	256
Average Influent pH (SU)	7.34	7.15	7.49	7.35
Average Effluent pH (SU)	7.35	7.27	7.73	7.46
Average Effluent DO (Number)	5.14	4.69	5.77	5.20
EFF BOD (mg/L)	3	3	3	3
EFF TSS (mg/L)	5.0	5.0	8	5.8
EFF NH3 (mg/L)	0.50	0.50	2	.57
EFF E-Coli (no/100ml)	10.0	10.0	10.0	10.0
Average MLSS (mg/L)	4287	3277	5093	4170
Average MLVSS (mg/L)	3223	2750	3810	3336
Average 30 Minute Sett. (ml/l)	770	630	877	797
Plant SVI (Number)	180	166	222	194
F:M Ratio	0.04	0.04	0.08	0.06
Sludge Age (days)	16.7	6.6	32.0	19.0

Sludge Disposal

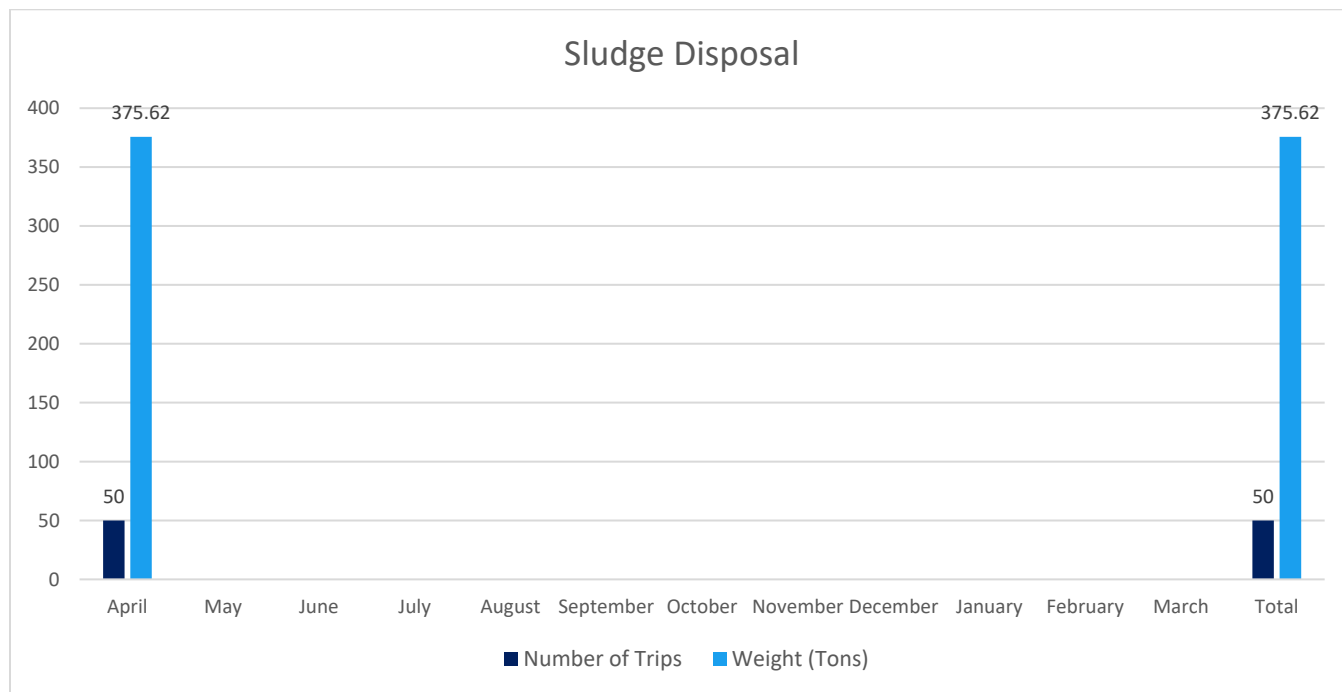

Cap Expenses

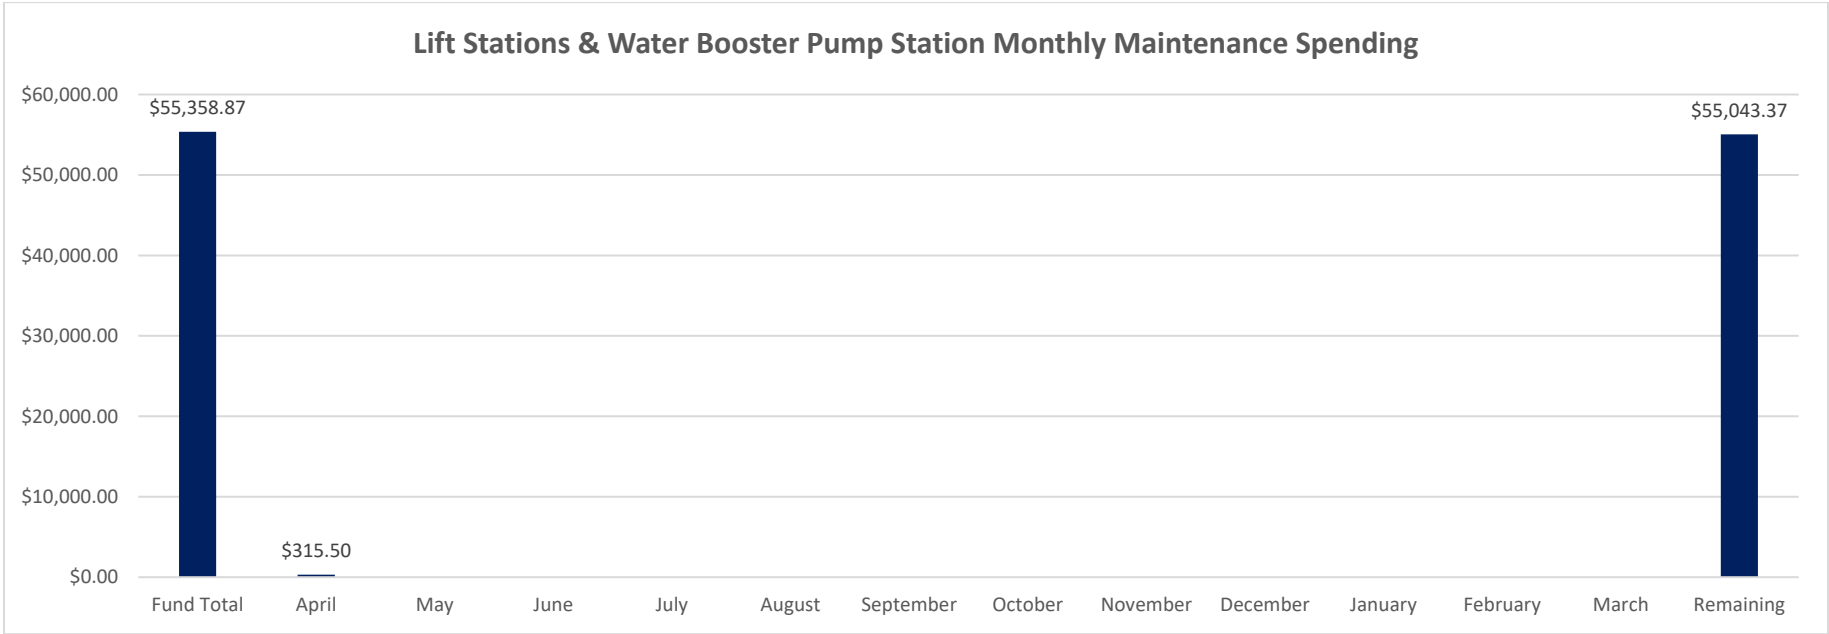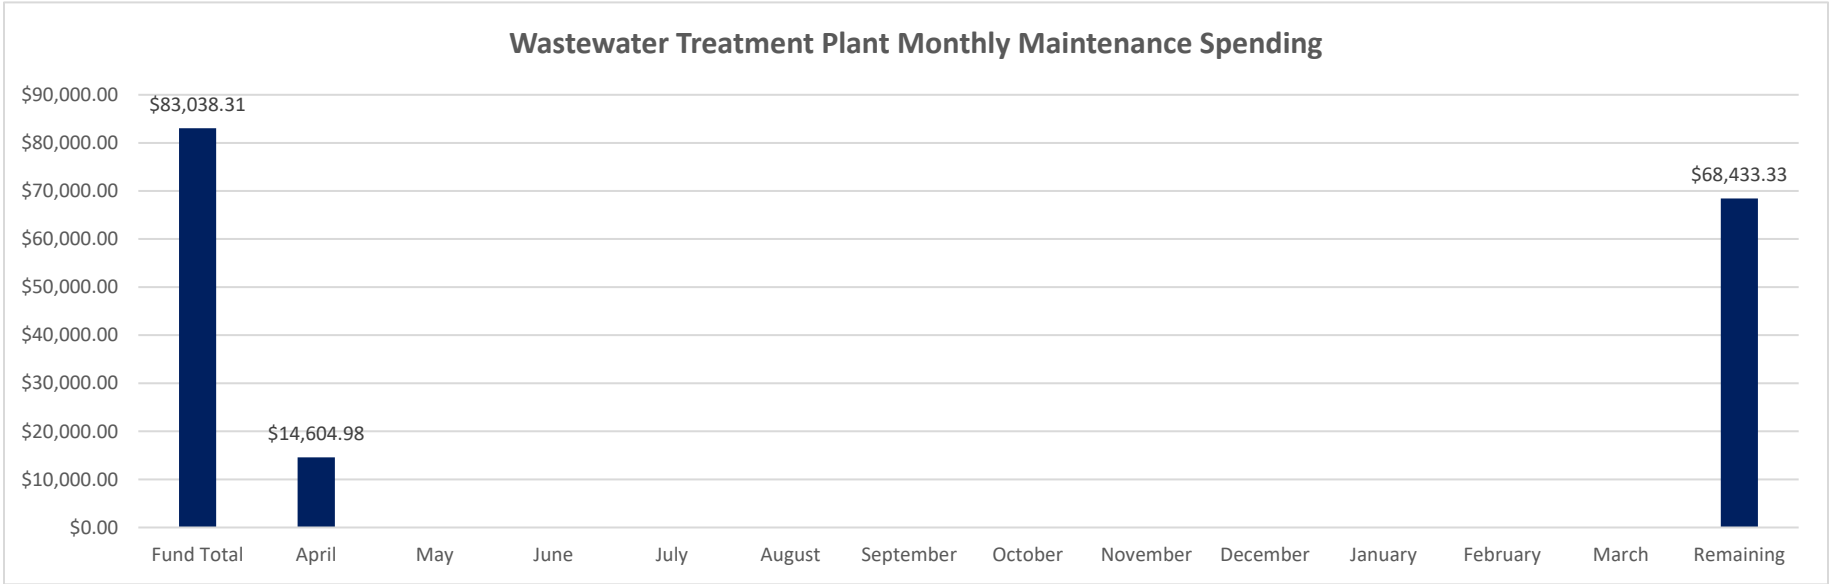

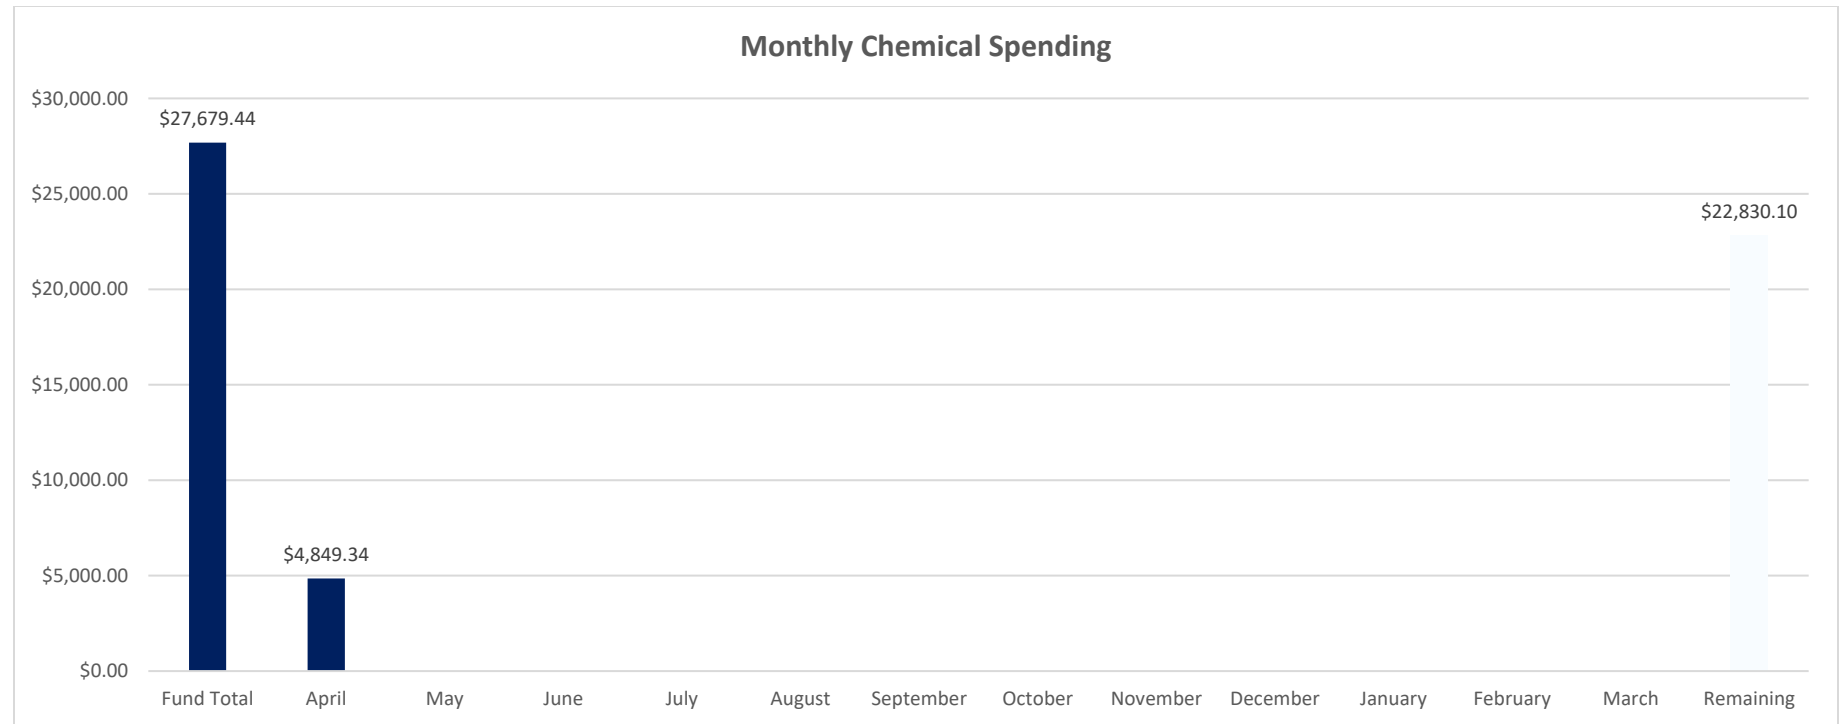

Regulatory Parameter Results

Date	Effluent BOD5	Effluent TSS	Influent BOD5	Influent TSS	E-Coli	BOD5 % Removal	TSS % Removal
4/7/2026	< 3*	< 5*	257	166	< 10*	98.83	96.99
4/10/2026	< 3*	8	232	108	< 10*	98.71	92.59
4/17/2026	< 3*	< 5*	154	221	< 10*	98.05	97.74
4/24/2026	< 3*	< 5*	139	167	< 10*	97.84	97.01

*Below Lowest Detectable Limits

Discharge Monitoring Report (DMR)

Parameter		Quantity or Loading		Units	Quality or Concentration			Units	No. Ex.	Frequency of Analysis	Sample Type
		Average	Maximum		Minimum	Average	Maximum				
BOD, 5 Day Effluent	Sample Measurement	56	*****	26 lbs/day	*****	3	3	19 mg/l	0	Weekly	COMP
	Permit Requirement	500.4 Monthly Average	*****		*****	30.0 Monthly Average	45.0 Weekly Average			Weekly	COMP
pH Effluent	Sample Measurement	*****	*****		7.27	*****	7.73	12 S.U.	0	Daily	GRAB
	Permit Requirement	*****	*****		6.5 Minimum	*****	9 Maximum			Daily	GRAB
TSS Effluent	Sample Measurement	106	*****	26 lbs/day	*****	5	8	19 Mg/l	0	Weekly	COMP
	Permit Requirement	500.4 Monthly Average	*****		*****	30.0 Monthly Average	45.0 Weekly Average			Weekly	COMP
Flow Effluent	Sample Measurement	1.659	3.073	03 MGD	*****	*****	*****		0	Daily	TOTAL
	Permit Requirement	REPORT Monthly Average	REPORT Maximum Daily		*****	*****	*****			Daily	TOTAL
E.coli Effluent	Sample Measurement	*****	*****		*****	10	10	3Z CFU/100mL	0	Weekly	GRAB
	Permit Requirement	*****	*****		*****	630 Geometric Mean	2030 Maximum Daily			Weekly	GRAB

Repair & Project Activity Photos

Kimberly Clark Lift Station sink hole



Rocks and debris inside the lift station pump



Impellor of the pump at Kimberly Clark Lift Station



Debris Removed from the pump and debris in the lift station



PUBLIC WORKS
MONTHLY REPORT

Consumer Confidence Report – 2026 Covering Calendar Year – 2025

JENKS PWA OK3007201

This report is a snapshot of the quality of the water that we provided last year. Included are the details about where your water comes from, what it contains, and how it compares to Environmental Protection Agency (EPA) and state standards. We are committed to providing you with information because informed customers are our best allies.

For access to the JENKS PWA service line inventory, or if you would like to be actively involved in the decision-making processes that affect drinking water quality, please call JENKS PWA at 918-299-5883.

Our drinking water is supplied from another water system through a Consecutive Connection (CC). To find out more about our drinking water sources and additional chemical sampling results, please contact our office at the number provided above. Your water comes from :

Buyer Name	Seller Name
JENKS PWA	TULSA

Some people may be more vulnerable to contaminants in drinking water than the general population. Immuno-compromised persons such as those with cancer undergoing chemotherapy, persons who have undergone organ transplants, people with HIV/AIDS or other immune system disorders, some elderly, and infants can be particularly at risk from infections. These people should seek advice about drinking water from their health care providers. EPA/CDC guidelines on appropriate means to lessen the risk of infection by *Cryptosporidium* and other microbial contaminants are available from the Safe Drinking Water Hotline (800-426-4791).

Drinking water, including bottled water, may reasonably be expected to contain at least small amounts of some contaminants. The presence of contaminants does not necessarily indicate that water poses a health risk. More information about contaminants and potential health effects can be obtained by calling the EPA's Safe Drinking Water Hotline (800-426-4791).

The sources of drinking water (both tap water and bottled water) include rivers, lakes, streams, ponds, reservoirs, springs, and wells. As water travels over the surface of the land or through the ground, it dissolves naturally occurring minerals and, in some cases, radioactive material, and can pick up substances resulting from the presence of animals or from human activity. Please contact us to obtain more information about a source water assessment and its availability.

Contaminants that may be present in source water before we treat it include:

Microbial contaminants, such as viruses and bacteria, which may come from sewage treatment plants, septic systems, livestock operations and wildlife.

Inorganic contaminants, such as salts and metals, which can be naturally-occurring or result from urban storm water runoff, industrial or domestic wastewater discharges, oil and gas production, mining or farming.

Pesticides and herbicides, which may come from a variety of sources such as storm water run-off, agriculture, and residential users.

Radioactive contaminants, which can be naturally occurring or the result of mining activity.

Organic contaminants, including synthetic and volatile organic chemicals, which are by-products of industrial processes and petroleum production, and also come from gas stations, urban storm water run-off, and septic systems.

In order to ensure that tap water is safe to drink, EPA prescribes regulations which limits the amount of certain contaminants in water provided by public water systems. We treat our water according to EPA's regulations. Food and Drug Administration regulations establish limits for contaminants in bottled water, which must provide the same protection for public health.

Our water system is required to test a minimum of 15 samples per month in accordance with the Total Coliform Rule for microbiological contaminants. Coliform bacteria are usually harmless, but their presence in water can be an indication of disease-causing bacteria. When coliform bacteria are found, special follow-up tests are done to determine if harmful bacteria are present in the water supply. If this limit is exceeded, the water supplier must notify the public.

Water Quality Data

The following tables list all of the drinking water contaminants which were detected during the 2025 calendar year. The presence of these contaminants does not necessarily indicate the water poses a health risk. Unless noted, the data presented in this table is from the testing done January 1- December 31, 2025. The state requires us to monitor for certain contaminants less than once per year because the concentrations of these contaminants are not expected to vary significantly from year to year. Some of the data, though representative of the water quality, is more than one year old.

Terms & Abbreviations

Maximum Contaminant Level Goal (MCLG): the "Goal" is the level of a contaminant in drinking water below which there is no known or expected risk to human health. MCLGs allow for a margin of safety.

Maximum Contaminant Level (MCL): the "Maximum Allowed" MCL is the highest level of a contaminant that is allowed in drinking water. MCLs are set as close to the MCLGs as feasible using the best available treatment technology.

Secondary Maximum Contaminant Level (SMCL): recommended level for a contaminant that is not regulated and has no MCL.

Action Level (AL): the concentration of a contaminant that, if exceeded, triggers treatment or other requirements.

Treatment Technique (TT): a required process intended to reduce levels of a contaminant in drinking water.

Maximum Residual Disinfectant Level (MRDL): the highest level of a disinfectant allowed in drinking water. There is convincing evidence that addition of a disinfectant is necessary for control of microbial contaminants.

Non-Detects (ND): lab analysis indicates that the contaminant is not present.

Parts per Million (ppm) or milligrams per liter (mg/l)

Parts per Billion (ppb) or micrograms per liter (µg/l)

Picocuries per Liter (pCi/L): a measure of the radioactivity in water.

Millirems per Year (mrem/yr): measure of radiation absorbed by the body.

Monitoring Period Average (MPA): An average of sample results obtained during a defined time frame, common examples of monitoring periods are monthly, quarterly and yearly.

Nephelometric Turbidity Unit (NTU): a measure of the clarity of water. Turbidity in excess of 5 NTU is just noticeable to the average person. Turbidity is not regulated for groundwater systems.

Running Annual Average (RAA): an average of sample results obtained over the most current 12 months and used to determine compliance with MCLs.

Locational Running Annual Average (LRAA): Average of sample analytical results for samples taken at a particular monitoring location during the previous four calendar quarters.

Monitoring and Reporting (M/R): a violation for failure to conduct regular monitoring of drinking water quality or to submit monitoring results in a timely fashion.

Operational Evaluation Level (OEL): a report triggered by the disinfection by-products rule.

Testing Results for: JENKS PWA

Please Note: Because of sampling schedules, results may be older than 1 year

Microbiological	Result	MCL	MCLG	Typical Source
COLIFORM (TCR)	In the month of November, 2 sample(s) returned as positive	Treatment Technique Trigger	0	Naturally present in the environment

Disinfection Byproducts	Monitoring Period	Highest RAA	Range (low/high)	Unit	MCL	MCLG	Typical Source
TOTAL HALOACETIC ACIDS (HAA5)	2024	19	12.1 - 19.2	ppb	60	0	By-product of drinking water disinfection
TTHM	2024	48	48.2	ppb	80	0	By-product of drinking water disinfection

Lead and Copper	Monitoring Period	90 th Percentile	Range (low/high)	Unit	AL	Sites Over AL	Typical Source
COPPER, FREE	2021 - 2023	0.654	0.0151 - 0.892	ppm	1.3	0	Corrosion of household plumbing systems; Erosion of natural deposits; Leaching from wood preservatives.
LEAD	2021 - 2023	1.1	0 - 5.6	ppb	15	0	Corrosion of household plumbing systems; Erosion of natural deposits.

If present, elevated levels of lead can cause serious health problems, especially for pregnant women and young children. Lead in drinking water is primarily from materials and components associated with service lines and home plumbing. Your water system is responsible for providing high quality drinking water, but cannot control the variety of materials used in plumbing components. When your water has been sitting for several hours, you can minimize the potential for lead exposure by flushing your tap for 30 seconds to 2 minutes before using water for drinking or cooking. If you are concerned about lead in your water, you may wish to have your water tested. Information on lead in drinking water, testing methods, and steps you can take to minimize exposure is available from the Safe Drinking Water Hotline or at <http://www.epa.gov/safewater/lead>.

Chlorine/Chloramines Maximum Disinfection Level	MPA	MPA Units	RAA	RAA Units
12/01/2025 - 12/31/2025	2	MG/L	2.0	MG/L
01/01/2025 - 01/31/2025	3	MG/L	2.3	MG/L

During the 2025 calendar year, we had the below noted violation(s) of drinking water regulations.

Compliance Period	Analyte	Comments
1/1/2025 - 12/31/2025	DBP STAGE 2	MONITORING, ROUTINE (DBP), MAJOR

Additional Required Health Effects Language:

Coliforms are bacteria that are naturally present in the environment and are used as an indicator that other, potentially-harmful, bacteria may be present. Coliforms were found in more samples than allowed and this was a warning of potential problems.

Some or all of our drinking water is supplied from another water system. The table below lists all of the drinking water contaminants, which were detected during the 2025 calendar year from the water systems that we purchase drinking water from.

Regulated Contaminants	Collection Date	Water System	Highest Value	Range (low/high)	Unit	MCL	MCLG	Typical Source
ATRAZINE	1/28/2025	TULSA	0.335	0 - 0.335	ppb	3	3	Runoff from herbicide used on row crops
BARIUM	1/4/2022	TULSA	0.045	0.0394 - 0.045	ppm	2	2	Discharge of drilling wastes; Discharge from metal refineries; Erosion of natural deposits.
FLUORIDE	1/7/2025	TULSA	0.8	0.62 - 0.8	ppm	4	4	Natural deposits; Water additive which promotes strong teeth.

Secondary Contaminants	Collection Date	Water System	Highest Value	Range (low/high)	Unit	SMCL
CARBON, TOTAL	12/2/2025	TULSA	0.972	0.972	ppm	10000
SODIUM	10/7/2025	TULSA	9.71	9.07 - 9.71	MG/L	


During the 2025 calendar year, the water systems that we purchase water from had the below noted violation(s) of drinking water regulations.

Water System	Type	Category	Analyte	Compliance Period
No Violations Occurred in the Calendar Year of 2025				


Public Works Monthly Manhours Worked Summary

04/01/2026 to 04/30/2026

Departments	Manhours
Animal Control	0.00
Code Enforcement	0.00
Drainage	75.00
Emergency Management	0.00
Engineering	0.00
Facilities	4.00
Fleet Maintenance	0.00
General Maintenance / Other	3.00
Locates	0.00
Mowing	9.00
Oklahoma Aquarium	0.00
Parks / Recreation	323.00
Sewer	20.50
Street	121.00
Training	44.00
Water	504.67
WWTP	0.00
TOTAL	1104.17

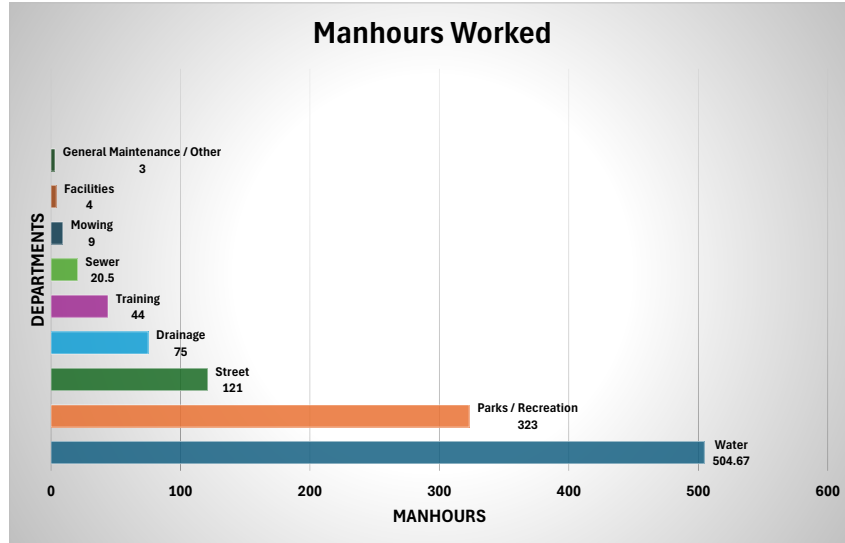

Departments	Tasks
Animal Control	0
Code Enforcement	0
Drainage	6
Emergency Management	0
Engineering	0
Facilities	2
Fleet Maintenance	0
General Maintenance / Other	1
Locates	0
Mowing	2
Oklahoma Aquarium	0
Parks / Recreation	24
Sewer	3
Street	23
Training	1
Water	88
WWTP	0
TOTAL	150

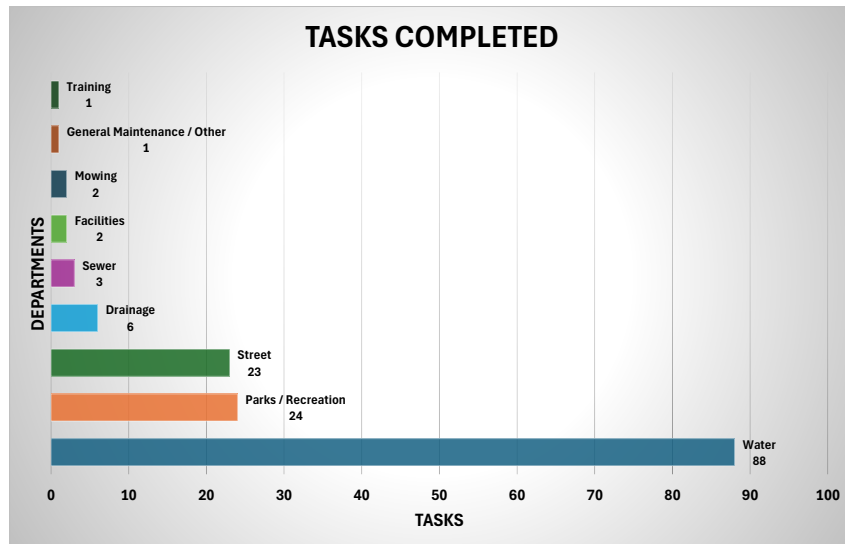

Public Works Monthly Closed Work Order Report

04/01/2026 to 04/30/2026

Completed Date	Task Name / Location / Work Order #	Asset Name	Time Spent
Group: Animal Control			
			Hours: 0
			Group Total: 0
Group: Code Enforcement			
			Hours: 0
			Group Total: 0
Group: Drainage			
04/08/2026	3712 W 106th St S (Grease / French Drain) - #32026	Drainage	2.00 hrs - Complete
04/09/2026	Drainage Clean Out - #32016	Drainage	40.00 hrs - Hauled a dump truck load of rock to site and put on sides of the drainage ditch. Leveled out and packed down.
04/13/2026	Check storm drains Westside - #32041	Drainage	4.00 hrs - Checked Westside storm drains
04/14/2026	Cleaned out trees and debris out of Storm Drains - #32083	Drainage	16.00 hrs - Cleaned out storm drains that had trees and debris in them. 6 bags
04/15/2026	STORM DRAIN WEEKLY CLEANING - #31865	Drainage	9.00 hrs - Checked and cleaned west storm drains and pumps 6 bags
04/24/2026	STORM DRAIN WEEKLY CLEANING - #32132	Drainage	4.00 hrs - Checked West storm drains and cleared. 5 bags
			Hours: 75
			Group Total: 6
Group: Emergency Management			
			Hours: 0
			Group Total: 0
Group: Engineering			
			Hours: 0
			Group Total: 0
Group: Facilities			
04/14/2026	Clean sidewalks at ranch - #32075	Facilities	1.00 hrs - Cleaned sidewalks and patio at the ranch
04/15/2026	Move desk / City Hall - #32093	Facilities	3.00 hrs - Move desk / City Hall
			Hours: 4
			Group Total: 2
Group: Fleet Maintenance			
			Hours: 0
			Group Total: 0
Group: General Maintenance / Other			
04/07/2026	Clean green sewer pump - #32020	General Maintenance / Other	3.00 hrs - Cleaned green sewer pump at shop
			Hours: 3
			Group Total: 1
Group: Locates			
			Hours: 0
			Group Total: 0
Group: Mowing			
04/13/2026	Mow ROW at slate creek - #32042	Mowing	3.00 hrs - Mowed bicycle trail between slate creek and oakwood
04/16/2026	Mowing - #32101	Mowing	6.00 hrs - Mowed and weedeated Alley behind Coney Island and Country Woods
			Hours: 9
			Group Total: 2
Group: Oklahoma Aquarium			
			Hours: 0
			Group Total: 0
Group: Parks / Recreation			
04/01/2026	Clean bathrooms at parks - #31994	Parks / Recreation	4.00 hrs - Clean bathrooms at parks
04/01/2026	Clean bathrooms at both parks - #31996	Parks / Recreation	1.00 hrs - Clean bathrooms at both parks
04/01/2026	Relocated Trees and shrubs - #31997	Parks / Recreation	43.00 hrs - Removed 3 trees and 3 shrubs for customers yard that they gave to the City and planted them at the Shop. Filled in holes at customers yard where we dug out the trees.
04/02/2026	TRASH PICK UP - IN TOWN LOCATIONS - #31981	Parks / Recreation	19.00 hrs - Picked up trash Downtown and Parks. 28 bags. Cleaned restrooms
04/02/2026	Down tree at Ranch - #32003	Parks / Recreation	13.00 hrs - Picked up tree that fell down at The Ranch. Hauled to Satellite yard and put in dumpster.
04/07/2026	Check trash at downtown main Street, parks, and pedestrian bridge - #32019	Parks / Recreation	15.00 hrs - Changed trash at downtown main Street, parks, and pedestrian bridge
04/09/2026	Herb & Plant Festival Banners - #32018	Parks / Recreation	23.00 hrs - Put up big banner Downtown
04/09/2026	Check sidewalks downtown main Street and clean bathrooms at both parks - #32036	Parks / Recreation	4.00 hrs - Checked sidewalks downtown main Street and cleaned bathrooms at both parks
04/10/2026	Downtown and Parks Trash - #32037	Parks / Recreation	9.00 hrs - Picked up trash Downtown and Parks. 41 bags Cleaned restrooms

Public Works Monthly Closed Work Order Report

04/01/2026 to 04/30/2026

Completed Date	Task Name / Location / Work Order #	Asset Name	Time Spent
04/13/2026	Downtown and Parks Trash - #32039	Parks / Recreation	19.00 hrs - Picked up trash Downtown and Parks. 40 bags Cleaned Restrooms
04/13/2026	Guards on trees at Outlet Mall - #32040	Parks / Recreation	4.00 hrs - Put plastic guards on bottoms of the trees along the back road behind the Mall.
04/15/2026	Received and moved Playground equipment - #32094	Parks / Recreation	6.00 hrs - Received Playground equipment at shop unloaded and took it to the Satellite Yard
04/15/2026	Trash Cans / Skate Park - #32095	Parks / Recreation	6.00 hrs - Removed 3 damaged trash cans at Skate Park and replaced with metal cans. Tried to clean up graffiti off and ordered parts to fix them.
04/16/2026	Moved Flower Pots / Hive Parking Lot - #32098	Parks / Recreation	4.00 hrs - Moved and rearranged large flower pots
04/17/2026	TRASH PICK UP - IN TOWN LOCATIONS - #32043	Parks / Recreation	24.00 hrs - Picked up trash Downtown and Parks 27 bags. Cleaned restrooms
04/20/2026	Downtown and Parks Trash - #32130	Parks / Recreation	20.00 hrs - Picked up trash Downtown and Parks 43 bags. Cleaned restrooms
04/21/2026	Air Freshers / Restrooms - #32136	Parks / Recreation	8.00 hrs - Installed new air fresheners in Commons and Veterans Parks restrooms
04/22/2026	Checked Downtown / Restrooms - #32143	Parks / Recreation	3.00 hrs - Checked Downtown trash and cleaned restrooms
04/23/2026	Graffiti at Veterans Park - #32145	Parks / Recreation	15.00 hrs - Painted the concrete walls that had graffiti. Also picked up limbs
04/24/2026	Downtown and Parks Trash - #32151	Parks / Recreation	6.00 hrs - Downtown and Parks trash 35 bags. Cleaned Restrooms
04/28/2026	Downtown and Parks Trash - #32161	Parks / Recreation	29.00 hrs - Picked up trash in Parks 40 bags
04/29/2026	Herb and Plant Festival Barricades and Sign Boards - #32131	Parks / Recreation	36.00 hrs - Took down all banners for Herb and Plant Festival
04/29/2026	Checked and Cleaned Restrooms - #32173	Parks / Recreation	3.00 hrs - Checked and cleaned restrooms at Commons Park and Veterans Park
04/30/2026	Trash and Restrooms - #32176	Parks / Recreation	9.00 hrs - Checked Downtown. Cleaned Commons and Veterans Parks restrooms. Picked up trash at Veterans Park 10 bags. Also had to call Jenk's PD on a homeless person camping out at the pavilion by the pond. They found drugs on him and he got arrested so had to g back and pick up trash that was left form homeless person 2 bags

Hours: 323

Group Total: 24

Group: Sewer

04/16/2026	Call Out / Skyline Pump / 12519 S 12th Street - #32102	Sewer	6.00 hrs - Customer called and said sewer was backing up. Went and checked / tripped breakers and pump started working. Going to get Jeff to come tomorrow and test breakers.
04/20/2026	Ozark Laser (Returned Sewer Plug/Ball) - #32126	Sewer	2.50 hrs - Complete
04/30/2026	Sewer Force Main Break / Harvard and 126th - #32174	Sewer	12.00 hrs - Borer hit our 6" Force Main Sewer line. Cut damaged pipe out and put 2 6" clamps on and a new pipe.

Hours: 20.5

Group Total: 3

Group: Street

04/03/2026	RUN TO THE WELL - #32004	Street	2.00 hrs
04/06/2026	SPECIAL EVENT BARRICADE & CONE PICK UP - #32195	Street	2.00 hrs
04/07/2026	Riverside Car Show Banner - #32017	Street	4.00 hrs - Put up Riverside Car Show Banner Downtown
04/08/2026	Fill in potholes at E 96th St & hwy 75 bridge - #32021	Street	12.00 hrs - Repaired potholes at E 96th St and hwy 75 bridge
04/09/2026	State Creek Cleanup - #32035	Street	10.00 hrs - Filled in around sidewalk ramp with dirt.
04/14/2026	504 E B St (25 mph sign) - #32076	Street	3.00 hrs - Complete
04/14/2026	Low limb 104th and Elwood - #32078	Street	4.00 hrs - Cut low hanging limb on Elwood at 104th street
04/14/2026	Barricades Road block by Sonic - #32081	Street	6.00 hrs - Put up barricades for road block because contractors busted a Gas Main. Blocked off Main St, Cedar, Birch, and A st. With type 3 barricades
04/14/2026	Potholes Main st and 75 bridge - #32082	Street	3.00 hrs - Filled in Potholes on Main st and 75 bridge 10 bags
04/16/2026	Pothole / Coney Island - #32100	Street	4.00 hrs - Filled in pothole in alley way behind Coney Island with one skid steer bucket of millings
04/17/2026	Planning Commission (121st & 33rd) - #32123	Street	3.00 hrs - Complete
04/20/2026	Picked up signage at Intersections - #32122	Street	11.00 hrs - Picked up more signs placed illegally at intersections. About 40 more signs
04/22/2026	Homeless Camp Cleanup / Elm and 101st - #32144	Street	3.00 hrs - Homeless Camp Cleanup / Elm and 101st Picked up trash and hauled to Satellite Dumpster 7 bags of trash
04/24/2026	Tree Down in Road - #32152	Street	10.00 hrs - Tree fell down in road. Cut up and hauled to the Satellite yard
04/27/2026	117th & Vine St (Playground sign) - #32155	Street	1.00 hrs - Complete
04/27/2026	138th Pl & 19th St (Stop sign) - #32156	Street	1.00 hrs - Complete
04/27/2026	SPECIAL EVENT BARRICADE & CONE PICK UP - #32159	Street	11.00 hrs - Picked up all barricades, cones, signs, and sign boards.
04/27/2026	118th St & Elwood Ave (Street name) - #32158	Street	1.00 hrs - Complete
04/27/2026	JENKS PLANT 'N' HERB FESTIVAL - BARRICADES & CONE - #32153	Street	10.00 hrs - Put out barricades,cones, and signs.
04/27/2026	George's Pub Sign / Fall Hazard - #32160	Street	6.00 hrs - Cut down George's Pub sign because it was about to fall down. Loaded on trailer and took to Satellite yard
04/29/2026	111th St & 2nd St (25mph sign) - #32167	Street	4.00 hrs - Complete
04/29/2026	131 St St & Kimberly Clark Ave (Stop Sign) - #32168	Street	4.00 hrs - Done

Public Works Monthly Closed Work Order Report

04/01/2026 to 04/30/2026

Completed Date	Task Name / Location / Work Order #	Asset Name	Time Spent
04/29/2026	Potholes - #32172	Street	6.00 hrs - Filled in Potholes at E 123rd Street 2 bags / 10735 N Douglas Street 6 bags
			Hours: 121
			Group Total: 23
Group: Training			
04/10/2026	Equipment Training - #32038	Training	44.00 hrs - Did Equipment Training
			Hours: 44
			Group Total: 1
Group: Water			
04/01/2026	421 N 7 st - #31998	Water	8.00 hrs
04/02/2026	918 N Ivy Place (Meter Can Raised) - #31916	Water	8.00 hrs
04/02/2026	Water leak 454 w 113 st s - #31881	Water	3.00 hrs
04/02/2026	Water leak 11621 s Primrose ct - #32000	Water	2.00 hrs - Fixed setter
04/02/2026	Pulled Meter at 917 w f st - #32001	Water	2.00 hrs - Took out meter
04/02/2026	Installing Meter at 917 w f st - #32002	Water	2.00 hrs - Reinstall meter
04/06/2026	511 W 114th St (Locate Water Meter) - #32015	Water	1.00 hrs - Complete
04/06/2026	JOB SITE CLEAN-UP 10721 master cir. (5 rolls of Fescue and dirt) - #31788	Water	4.00 hrs
04/06/2026	JOB SITE CLEAN-UP 2005 w 119th st s - #31781	Water	4.00 hrs
04/06/2026	JOB SITE CLEAN-UP 11708 S umber st - #31831	Water	2.00 hrs
04/06/2026	JOB SITE CLEAN-UP 1412 w 117 st s - #31955	Water	4.00 hrs
04/06/2026	JOB SITE CLEAN-UP 12105 s 14th ct - #31825	Water	4.00 hrs
04/06/2026	JOB SITE CLEAN-UP 11326 w 113th street - #31794	Water	0.02 hrs
04/07/2026	Water Samples @ COJ 04/07/26 - #32023	Water	13.00 hrs - Complete
04/07/2026	5th and b JOB SITE CLEAN-UP - #30336	Water	4.00 hrs
04/07/2026	JOB SITE CLEAN-UP 11326 w 113th st s - #31793	Water	2.00 hrs
04/07/2026	JOB SITE CLEAN-UP 311 w k st - #31798	Water	1.83 hrs
04/08/2026	1515 W 117th St (Water Leak) - #31947	Water	42.00 hrs
04/08/2026	111 s willow st - #32024	Water	2.00 hrs - Check out a leak
04/08/2026	12514 Ash Ave (low pressure) - #32022	Water	5.50 hrs - Complete
04/09/2026	12324 S Ash Ave - Lead Service Line Verification - #32028	Water	2.00 hrs
04/09/2026	LEAD SERVICE LINE VERIFICATION - 824 N 2 ST - #30048	Water	2.00 hrs
04/10/2026	LEAD SERVICE LINE VERIFICATION - 214 E H ST - #30055	Water	0.50 hrs
04/10/2026	LEAD SERVICE LINE VERIFICATION - 235 E H ST - #30057	Water	0.50 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 241 E H ST - #30056	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 223 E H ST - #30058	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 208 E H ST - #30054	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 204 E H ST - #30053	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 202 E H ST - #30052	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 113 E H ST - #30065	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 107 E H ST - #30064	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 108 E H ST - #30062	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 102 E H ST - #30063	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 903 N 1 ST - #30051	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 902 N 1 ST - #30050	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 104 W H ST - #30066	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 110 W H ST - #30067	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 240 E J ST - #30077	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 234 E J ST - #30076	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE REPLACE 228 e j st - #25216	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 222 E J ST - #30074	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 216 E J ST - #30073	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 204 E J ST - #30072	Water	0.67 hrs

Public Works Monthly Closed Work Order Report

04/01/2026 to 04/30/2026

Completed Date	Task Name / Location / Work Order #	Asset Name	Time Spent
04/14/2026	LEAD SERVICE LINE VERIFICATION - 108 E J ST - #30071	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 114 E J ST - #30070	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 111 E J ST - #30069	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE REPLACE 103 e j st - #32068	Water	0.02 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION-103 E J ST - #29712	Water	0.67 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 904 N 2 ST - #30049	Water	0.75 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 916 N 2 ST - #30079	Water	0.75 hrs
04/14/2026	LEAD SERVICE LINE VERIFICATION - 922 N 2 ST - #30080	Water	0.75 hrs
04/14/2026	JOB SITE CLEAN-UP 512 w. C st - #29937	Water	3.00 hrs - Added dirt and 4 rolls of Bermuda sod. Picked up barricades
04/15/2026	Clean up Crew- 922 N 2nd - #32085	Water	0.25 hrs - done
04/15/2026	Water leak 400 e Duncan st - #31970	Water	17.52 hrs
04/15/2026	12814 S Cedar. St (Meter lid cover) - #32090	Water	2.00 hrs - Complete
04/15/2026	13657 S 20th Pl (Meter lid) - #32092	Water	4.00 hrs - Complete
04/16/2026	11127 s ash - #32096	Water	6.00 hrs
04/16/2026	526 N Elm St (Water leak) - #32029	Water	8.00 hrs
04/16/2026	E 103 Starbucks - #32097	Water	5.00 hrs
04/17/2026	LEAD SERVICE LINE VERIFICATION - 1016 N 3 ST - #30083	Water	0.75 hrs
04/17/2026	LEAD SERVICE LINE VERIFICATION - 1004 N 3 ST - #30081	Water	0.75 hrs
04/17/2026	LEAD SERVICE LINE VERIFICATION - 1010 N 3 ST - #30082	Water	0.75 hrs
04/17/2026	LEAD SERVICE LINE VERIFICATION - 1028 N 3 ST - #30085	Water	0.75 hrs
04/17/2026	LEAD SERVICE LINE VERIFICATION - 116 W K PL - #30098	Water	0.75 hrs
04/17/2026	LEAD SERVICE LINE VERIFICATION - 112 W K PL - #30097	Water	0.75 hrs
04/17/2026	LEAD SERVICE LINE VERIFICATION - 108 W K PL - #30096	Water	0.75 hrs
04/17/2026	LEAD SERVICE LINE VERIFICATION - 1022 N 3 ST - #30084	Water	0.02 hrs
04/17/2026	LEAD SERVICE LINE VERIFICATION - 1027 N 1 ST - #30106	Water	0.75 hrs
04/17/2026	LEAD SERVICE LINE VERIFICATION - 1021 N 1 ST - #30107	Water	0.77 hrs
04/17/2026	LEAD SERVICE LINE VERIFICATION - 1015 N 1 ST - #30108	Water	0.75 hrs
04/17/2026	LEAD SERVICE LINE VERIFICATION - 1008 N 1 ST - #30103	Water	0.75 hrs
04/17/2026	LEAD SERVICE LINE VERIFICATION - 920 N 1 ST - #30101	Water	0.75 hrs
04/17/2026	LEAD SERVICE LINE VERIFICATION - 914 N 1 ST - #30100	Water	0.75 hrs
04/17/2026	LEAD SERVICE LINE VERIFICATION - 908 N 1 ST - #30099	Water	0.75 hrs
04/17/2026	LEAD SERVICE LINE VERIFICATION - 909 N 1 ST - #30105	Water	0.75 hrs
04/21/2026	Water Samples (COJ 04/21/26) - #32133	Water	6.50 hrs - Complete
04/22/2026	Riverwalk - #32141	Water	24.00 hrs
04/24/2026	Water leak repair 2722 e 140th pl s - #32148	Water	8.00 hrs
04/24/2026	13331 s 20th pl - #32149	Water	8.00 hrs
04/24/2026	Meter swap 438 e 130th st - #32150	Water	4.00 hrs
04/25/2026	118 south Elm st - #31993	Water	208.00 hrs
04/27/2026	Raise fire hydrant a and cedar - #32157	Water	32.00 hrs
04/28/2026	LEAD SERVICE LINE VERIFICATION - 1004 N 2 ST - #30095	Water	4.00 hrs
04/28/2026	LEAD SERVICE LINE VERIFICATION - 1010 N 2 ST - #30094	Water	4.00 hrs
04/29/2026	LEAD SERVICE LINE REPLACE 1813 n ash - #24514	Water	0.08 hrs
04/29/2026	LEAD SERVICE LINE VERIFICATION - 1005 N 2 ST - #30086	Water	4.00 hrs
04/29/2026	LEAD SERVICE LINE VERIFICATION - 1011 N 2 ST - #30087	Water	4.00 hrs
04/29/2026	LEAD SERVICE LINE VERIFICATION - 1017 N 2 ST - #30088	Water	4.00 hrs
			Hours: 504.67

Public Works Monthly Closed Work Order Report			
04/01/2026 to 04/30/2026			
Completed Date	Task Name / Location / Work Order #	Asset Name	Time Spent
			Group Total: 88
Group: WWTP			
			Hours: 0
			Group Total: 0
			Total Hours: 1104.67
			Total Tasks: 150

ENGINEERING
MONTHLY REPORT

PROJECTS STATUS REPORTS

Date of update: May 29, 2026

Bold italicized notes are changes/additions from the previous report

Strike through indicates item is complete

Streets Projects

Elm/Turnpike Interchange

Construction completed March 2017

Right-of-way acquisition still ongoing.

Elwood Avenue (Main to 111th Street)

Phase I, Phase 2 and Phase 3 project approved for ODOT STP funding

Projected schedule:

Engineering Contract Awarded	October 2013
Preliminary Design Complete	March 2014
Final Design Complete	March 2024
Environmental Complete	February 2017
Right-of-way Acquisition Complete	December 2022
Utility Relocation Complete	February 2027
Bid Project	February 2027
Award of Contract	March 2027
Construction Complete	October 2029

S. Elm Street Improvements (111th Street to 121st Street)

Projected schedule:

Engineering Contract Awarded	May 2016
Preliminary Design Complete	July 2017
Final Design Complete	October 2022
Environmental Complete	Not Applicable
Right-of-way Acquisition Complete	May 2024
Utility Relocation Complete	December 2023
Bid Project	October 2024
Award of Contract	November 2024
Construction Complete	January 2027

S. Elm Street Improvements (121th Street to 131st Street)

Projected schedule:

Engineering Contract Awarded	May 2016
Preliminary Design Complete	July 2017
Final Design Complete	October 2022
Environmental Complete	Not Applicable
Right-of-way Acquisition Complete	May 2024
Utility Relocation Complete	March 2026
Bid Project	March 2026
Award of Contract	April 2026
Construction Complete	July 2027

Streets Projects (continued)**106th Street (Elm to River District)**Projected schedule:

Engineering Contract Awarded	July 2021
Preliminary Design Complete	June 2026
Final Design Complete	September 2026
Environmental Complete	October 2026
Right-of-way Acquisition Complete	October 2026
Utility Relocation Complete	October 2026
Bid Project	January 2027
Award of Contract	February 2027
Construction Complete	February 2028

Elwood Avenue (91st to 96th Street)Projected schedule:

Engineering Contract Awarded	July 2022
Preliminary Design Complete	January 2023
Final Design Complete	August 2023
Environmental Complete	
Right-of-way Acquisition Complete	ON HOLD
Utility Relocation Complete	
Bid Project	
Award of Contract	
Construction Complete	

Elwood Avenue (111th to 121st Street)Projected schedule:

Engineering Contract Awarded	July 2022
Preliminary Design Complete	January 2023
Final Design Complete	December 2023
Environmental Complete	ON HOLD
Right-of-way Acquisition Complete	
Utility Relocation Complete	
Bid Project	
Award of Contract	
Construction Complete	

121st Street (Elm Street to Elwood Avenue) TrailProjected schedule:

Engineering Contract Awarded	September 2023
Preliminary Design Complete	January 2024
Final Design Complete	April 2025
Environmental Complete	February 2025
Right-of-way Acquisition Complete	Not Applicable
Utility Relocation Complete	December 2025
Bid Project	October 2025
Award of Contract	November 2025
Construction Complete	September 2026

Streets Projects (continued)**Pedestrian Bridge Rehabilitation****Projected schedule:**

Engineering Contract Awarded	April 2026
Preliminary Design Complete	August 2026
Final Design Complete	March 2027
Environmental Complete	
Right-of-way Acquisition Complete	
Utility Relocation Complete	
Bid Project	
Award of Contract	
Construction Complete	
Award of Contract	
Construction Complete	

N. 5th St. Sidewalk Extension**Projected schedule:**

Engineering Contract Awarded	December 2025
Preliminary Design Complete	
Final Design Complete	
Environmental Complete	
Right-of-way Acquisition Complete	
Utility Relocation Complete	
Bid Project	
Award of Contract	
Construction Complete	
Award of Contract	
Construction Complete	

Parkwest Trail Extension**Projected schedule:**

Engineering Contract Awarded	December 2025
Preliminary Design Complete	
Final Design Complete	
Environmental Complete	
Right-of-way Acquisition Complete	
Utility Relocation Complete	
Bid Project	
Award of Contract	
Construction Complete	
Award of Contract	
Construction Complete	

Sanitary Sewer Projects**106th and Elm Street Lift Station and Forcemain****Projected schedule:**

Engineering Contract Awarded	March 2021
Preliminary Design Complete	January 2024
Final Design Complete	August 2026
Environmental Complete	
Right-of-way Acquisition Complete	
Utility Relocation Complete	
Bid Project	
Award of Contract	
Construction Complete	

Sanitary Sewer Projects (continued)**Victoria Pond Lift Station and Forcemain**Projected schedule:

Engineering Contract Awarded	December 2021
Preliminary Design Complete	August 2022
Final Design Complete	August 2026
Environmental Complete	
Right-of-way Acquisition Complete	
Utility Relocation Complete	
Bid Project	
Award of Contract	
Construction Complete	

Water System Projects**121st Street Water Extension (Eddington Place to 27 W. Avenue)**Projected schedule:

Engineering Contract Awarded	September 2021
Preliminary Design Complete	May 2022
Final Design Complete	March 2024
Environmental Complete	Not Applicable
Right-of-way Acquisition Complete	May 2026
Utility Relocation Complete	Not Applicable
Bid Project	July 2026
Award of Contract	August 2026
Construction Complete	April 2027

Pedestrian Bridge Waterline ReplacementProjected schedule:

Engineering Contract Awarded	April 2023
Preliminary Design Complete	May 2023
Final Design Complete	June 2024
Environmental Complete	ON HOLD
Right-of-way Acquisition Complete	Not Applicable
Utility Relocation Complete	Not Applicable
Bid Project	ON HOLD
Award of Contract	ON HOLD
Construction Complete	ON HOLD

Water System Master PlanProjected schedule:

Engineering Contract Awarded	March 2026
Preliminary Design Complete	September 2026
Final Design Complete	January 2027
Environmental Complete	
Right-of-way Acquisition Complete	
Utility Relocation Complete	
Bid Project	
Award of Contract	
Construction Complete	

Drainage System Projects

Arkansas Riverbank (Main Street Bridge to Creek Turnpike Bridge) Stabilization Design

Projected schedule:

Engineering Contract Awarded	April 2022
Preliminary Design Complete	June 2022
Final Design Complete	ON HOLD
Environmental Complete	
Right-of-way Acquisition Complete	
Utility Relocation Complete	
Bid Project	
Award of Contract	
Construction Complete	

Elm/Turnpike Interchange Compensatory Storage

Projected schedule:

Engineering Contract Awarded	March 2026
Preliminary Design Complete	May 2026
Final Design Complete	July 2026
Environmental Complete	July 2026
Right-of-way Acquisition Complete	N/A
Utility Relocation Complete	N/A
Bid Project	October 2026
Award of Contract	November 2026
Construction Complete	April 2027

Vision 2025 Extension Projects

"C" Street (Fir to Elm Street) Sidewalk

Project schedule:

Engineering Contract Awarded	June 2023
Preliminary Design Complete	November 2023
Final Design Complete	March 2024
Environmental Complete	Not Applicable
Right-of-way Acquisition Complete	November 2024
Utility Relocation Complete	Not Applicable
Bid Project	ON HOLD
Award of Contract	
Construction Complete	

RAISE Grant Project

Tulsa-Jenks Multi-Modal Safety RAISE Project

Project schedule:

Engineering Contract Awarded	June 2024
Preliminary Design Complete	May 2025
Final Design Complete	January 2026
Environmental Complete	April 2026
Right-of-way Acquisition Complete	August 2026
Utility Relocation Complete	June 2026
Bid Project	September 2026
Award of Contract	December 2026
Construction Complete	January 2028

Engineering Department Projects

Aquarium Drive ("B" to Elm St.) and Elm Street (101st to 111th St.) Trail Rehabilitation

Projected schedule:

Engineering Contract Awarded	Not Applicable
Preliminary Design Complete	March 2024
Final Design Complete	June 2026
Environmental Complete	June 2026
Right-of-way Acquisition Complete	Not Applicable
Utility Relocation Complete	Not Applicable
Bid Project	October 2026
Award of Contract	November 2026
Construction Complete	April 2027

City Facility Projects

Fire Station No. 1

Projected schedule:

Engineering Contract Awarded	May 2020
Preliminary Design Complete	May 2023
Final Design Complete	February 2024
Environmental Complete	Not Applicable
Right-of-way Acquisition Complete	Not Applicable
Utility Relocation Complete	Not Applicable
Bid Project	March 2024
Award of Contract	May 2024
Construction Complete	June 2026

PROJECT STATUS SCHEDULE GANTT CHART
City of Jenks

Origin Date: 1/6/21
Date of update: May 29, 2026

Description	Status	Proposed Completion Month	2024				2025				2026				2027				2028									
			Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2						
			Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec						
			FY 2023				FY 2024				FY 2025				FY 2026				FY 2027				FY 2028					
STREET PROJECTS																												
Elm/Turnpike Interchange																												
Construction completed	Complete	March 2017																										
Right-of-way acquisition	In Progress	Ongoing																										
Elwood Avenue (Main to 111th Street) - Phase I																												
Engineering Contract Awarded	Complete	October 2013																										
Preliminary Design Complete	Complete	March 2014																										
Final Design Complete	Complete	March 2024																										
Environmental Complete	Complete	February 2017																										
Right-of-way Acquisition Complete	Complete	December 2022																										
Utility Relocation Complete	In Progress	February 2027																										
Bid Project		February 2027																										
Award of Contract		March 2027																										
Construction Complete		October 2029																										
S. Elm Street Improvements (111th Street to 121st Street)																												
Engineering Contract Awarded	Complete	May 2016																										
Preliminary Design Complete	Complete	July 2017																										
Final Design Complete	Complete	October 2022																										
Environmental Complete		Not Applicable																										
Right-of-way Acquisition Complete	Complete	May 2024																										
Utility Relocation Complete	Complete	December 2023																										
Bid Project	Complete	October 2024																										
Award of Contract	Complete	November 2024																										
Construction Complete	In Progress	January 2027																										
S. Elm Street Improvements (121th Street to 131st Street)																												
Engineering Contract Awarded	Complete	May 2016																										
Preliminary Design Complete	Complete	July 2017																										
Final Design Complete	Complete	October 2022																										
Environmental Complete		Not Applicable																										
Right-of-way Acquisition Complete	Complete	May 2024																										
Utility Relocation Complete	Complete	March 2026																										
Bid Project	Complete	March 2026																										
Award of Contract	Complete	April 2026																										
Construction complete		July 2027																										
106th Street (Elm to River District) Design																												
Engineering Contract Awarded	Complete	July 2021																										
Preliminary Design Complete	In Progress	June 2026																										
Final Design Complete		September 2026																										
Environmental Complete		October 2026																										
Right-of-way Acquisition Complete		October 2026																										
Utility Relocation Complete		October 2026																										
Bid Project		January 2027																										
Award of Contract		February 2027																										
Construction complete		February 2028																										

Description	Status	Proposed Completion Month	2024				2025				2026				2027				2028								
			Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2					
			Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec					
			FY 2023		FY 2024				FY 2025				FY 2026				FY 2027				FY 2028						
STREET PROJECTS (continued)																											
Elwood Avenue (91st to 96th Street) Design																											
Engineering Contract Award	Complete	July 2022																									
Preliminary Design Complete	Complete	January 2023																									
Final Design Complete	Complete	August 2023																									
Environmental Complete																											
Rights-of-way Acquisition Complete	ON HOLD	ON HOLD																									
Utility Relocation Complete																											
Bid Project																											
Award of Contract																											
Construction Complete																											
Elwood Avenue (111th to 121st Street) Design																											
Engineering Contract Award	Complete	July 2022																									
Preliminary Design Complete	Complete	January 2023																									
Final Design Complete	Complete	December 2023																									
Environmental Complete	ON HOLD	ON HOLD																									
Rights-of-way Acquisition Complete																											
Utility Relocation Complete																											
Bid Project																											
Award of Contract																											
Construction Complete																											
PARK-TRAIL-SIDEWALK PROJECTS																											
121st Street (Elm Street to Elwood Avenue) Trail																											
Engineering Contract Award	Complete	September 2023																									
Preliminary Design Complete	Complete	January 2024																									
Final Design Complete	Complete	April 2025																									
Environmental Complete	Complete	February 2025																									
Rights-of-way Acquisition Complete		Not Applicable																									
Utility Relocation Complete	Complete	December 2025																									
Bid Project	Complete	October 2025																									
Award of Contract	Complete	November 2025																									
Construction Complete	In Progress	September 2026																									
Pedestrian Bridge Rehabilitation																											
Engineering Contract Award	Complete	April 2026																									
Preliminary Design Complete	In Progress	August 2026																									
Final Design Complete		March 2027																									
Environmental Complete																											
Rights-of-way Acquisition Complete																											
Utility Relocation Complete																											
Bid Project																											
Award of Contract																											
Construction Complete																											

Description	Status	Proposed Completion Month	2024				2025				2026				2027				2028			
			Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
			Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec
			FY 2023		FY 2024		FY 2025		FY 2026		FY 2027		FY 2028									
SANITARY SEWER & WATER LINE PROJECTS (continued)																						
121st Street Waterline Extension (Eddington Place to 27 W. Avenue)																						
Engineering Contract Award	Complete	September 2021																				
Preliminary Design Complete	Complete	May 2022																				
Final Design Complete	Complete	March 2024																				
Environmental Complete		Not Applicable																				
Rights-of-way Acquisition Complete		May 2026																				
Utility Relocation Complete		Not Applicable																				
Bid Project		July 2026																				
Award of Contract		August 2026																				
Construction Complete		April 2027																				
Pedestrian Bridge Waterline Replacement																						
Engineering Contract Award	Complete	April 2023																				
Preliminary Design Complete	Complete	May 2023																				
Final Design Complete	Complete	June 2024																				
Environmental Complete		On Hold																				
Rights-of-way Acquisition Complete		Not Applicable																				
Utility Relocation Complete		Not Applicable																				
Bid Project		ON HOLD																				
Award of Contract		ON HOLD																				
Construction Complete		ON HOLD																				
Water System Master Plan																						
Engineering Contract Award	Complete	March 2026																				
Preliminary Design Complete	In Progress	September 2026																				
Final Design Complete		January 2027																				
Environmental Complete																						
Rights-of-way Acquisition Complete																						
Utility Relocation Complete																						
Bid Project																						
Award of Contract																						
Construction Complete																						
DRAINAGE SYSTEM PROJECTS																						
Arkansas Riverbank (Main St. Bridge to Creek Turnpike Bridge) Stabilization																						
Engineering Contract Award	Complete	April 2022																				
Preliminary Design Complete	Complete	June 2022																				
Final Design Complete	In Progress	ON HOLD																				
Environmental Complete																						
Rights-of-way Acquisition Complete																						
Utility Relocation Complete																						
Bid Project																						
Award of Contract																						
Construction Complete																						

Description	Status	Proposed Completion Month	2024				2025				2026				2027				2028			
			Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
			Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec
			FY 2023			FY 2024			FY 2025			FY 2026			FY 2027			FY 2028				
DRAINAGE SYSTEM PROJECTS (continued)																						
Elm/Turnpike Interchange Compensatory Storage																						
Engineering Contract Award	Complete	March 2026																				
Preliminary Design Complete	In Progress	May 2026																				
Final Design Complete		July 2026																				
Environmental Complete		July 2026																				
Rights-of-way Acquisition Complete		N/A																				
Utility Relocation Complete		N/A																				
Bid Project		October 2026																				
Award of Contract		November 2026																				
Construction Complete		April 2027																				
VISION 2025 EXTENSION PROJECTS																						
"C" Street (Fir to Elm Street) Sidewalk																						
Engineering Contract Award	Complete	June 2023																				
Preliminary Design Complete	Complete	November 2023																				
Final Design Complete	Complete	March 2024																				
Environmental Complete		Not Applicable																				
Rights-of-way Acquisition Complete	In Progress	November 2024																				
Utility Relocation Complete		Not Applicable																				
Bid Project		ON HOLD																				
Award of Contract																						
Construction Complete																						
RAISE GRANT PROJECT																						
Tulsa-Jenks Multi-Modal Safety RAISE Project																						
Engineering Contract Award	Complete	June 2024																				
Preliminary Design Complete	Complete	May 2025																				
Final Design Complete	Complete	January 2026																				
Environmental Complete	Complete	April 2026																				
Rights-of-way Acquisition Complete	In Progress	August 2026																				
Utility Relocation Complete		June 2026																				
Bid Project		September 2026																				
Award of Contract		December 2026																				
Construction Complete		January 2028																				
ENGINEERING DEPARTMENT PROJECTS																						
Aquarium Drive ("B" to Elm St.) and Elm Street (101st to 111th St.) Trail Rehabilitation																						
Engineering Contract Award		Not Applicable																				
Preliminary Design Complete	Complete	March 2024																				
Final Design Complete	In Progress	June 2026																				
Environmental Complete	In Progress	June 2026																				
Rights-of-way Acquisition Complete		Not Applicable																				
Utility Relocation Complete		Not Applicable																				
Bid Project		October 2026																				
Award of Contract		November 2026																				
Construction Complete		April 2027																				

Description	Status	Proposed Completion Month	2024				2025				2026				2027				2028							
			Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2				
			Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sep	Oct-Dec				
			FY 2023		FY 2024				FY 2025				FY 2026				FY 2027				FY 2028					
CITY FACILITY PROJECTS																										
Fire Station No. 1																										
Engineering Contract Award	Complete	May 2020																								
Preliminary Design Complete	Complete	May 2023																								
Final Design Complete	Complete	February 2024																								
Environmental Complete		Not Applicable																								
Rights-of-way Acquisition Complete		Not Applicable																								
Utility Relocation Complete		Not Applicable																								
Bid Project	Complete	March 2024																								
Award of Contract	Complete	April 2024																								
Construction Complete	In Progress	June 2026																								

RESIDENTIAL DEVELOPMENT STATUS SHEET
City of Jenks Engineering Department

Revised: 5/29/2026

Development	Pre-Develop Meeting	SWP3	Earth Change Permit	Start Earth Work	Construction Plans Accepted			ODHQ Permit Issued		Pre-Const. Meeting	Construction Complete					Punch List		Maintenance						
					Water Line	Sanitary Sewer	Street & Drainage	Water Line	Sanitary Sewer		Sanitary Sewer	Water	Drainage	Street	Generated	Complete	Bonds Provided	City Council Accept	Contractor Evaluation Complete	Maint. Period Insp. (10 Mo.)	1 Year Inspection Complete	Mailed 1 Year Punch List	Mailed Second 1 Year Punch List	1 Year Punch List Complete
Frazier Meadows Phase II	2/20/24	3/12/19	8/29/24	9/2/24	11/22/24	5/7/21	7/8/25	4/9/21	4/9/21	9/2/24	6/5/23	7/8/25	7/8/25	5/9/25	6/9/25	7/8/25	7/8/25	7/15/25		5/15/26				
Frazier Falls	11/23/21	11/3/25	12/5/25	12/15/25						12/11/25														
Estates at Ritz Hollow	3/1/21	8/4/21	8/18/21	1/3/22	6/23/22	6/23/22	8/18/21	4/13/22	6/3/22	6/13/22	12/1/22	9/26/22	9/1/23	6/1/23	9/21/23	9/29/23	8/23/23	9/19/23		7/19/24				
Harvard Oaks	12/6/21	9/13/22	9/21/22	1/9/23	3/28/23	3/28/23	9/5/23	3/21/23	3/21/23	4/24/23	6/30/23	9/1/23	12/29/23	12/29/23	11/21/24		3/4/24	12/17/24		10/17/25				
Reserve @ Southern Woods	4/22/24	8/7/24	8/27/24	8/27/24	11/22/24	11/22/24		12/30/24	12/30/24	8/27/24	1/16/26	1/16/26	1/16/26	1/16/26	1/22/26									
Elm Crossing (121st and Elm [Shaw])	3/9/22	10/15/24	5/20/25(PA)	6/23/25						6/19/25														
Crossvine (128th and Elm)	10/30/23																							
Glenwood Ridge (McGuire)	7/27/23																							
Kimberly Estates (131st and Harvard)	12/3/24	12/22/25	12/22/25	1/5/26			5/15/26			12/22/25														
Belvedere Estates (131st and Harvard)	10/23/24	11/4/25	11/21/25	11/24/25	4/10/26	4/10/26	4/10/26	4/17/26	4/17/26	11/21/25														
Bentley Ranch (131st and Elm)	10/28/24	11/10/25	12/5/25	12/8/25						12/5/25														
The Hideaway (136th Pl. and Harvard)	12/9/25																							

COMMERCIAL DEVELOPMENT STATUS SHEET
City of Jenks Engineering Department

Revised: 5/29/2026

Development	Pre-Develop Meeting	SWP3	Earth Change Permit	Start Earth Work	Construction Phase Accepted			ODJQ Permit Issued			Construction Complete				Punch List		Maintenance							
					Water Line	Sanitary Sewer	Street & Drainage	Water Line	Sanitary Sewer	Pre-Const. Meeting	Sanitary Sewer	Water	Drainage	Street	Generated	Complete	Bonds Provided	City Council Accept	Contractor Evaluation Complete	Maint. Period Insp. (10 Mo.)	1 Year Inspection Complete	Mailed 1 Year Punch List	Mailed Second 1 Year Punch List	1 Year Punch List Complete
South County Crossing II		1/26/2022	1/24/22	3/10/22	1/24/22	8/15/22	N/A	8/15/22	8/11/22	8/22/22	10/7/22		12/28/22	12/28/22	N/A	N/A								
SH 117 Development		1/7/2021	2/1/21	5/4/21	N/A	N/A	12/1/21																	
Eighteen Acres Ranch		8/9/2022	7/22/22	9/28/22	10/18/23	N/A	N/A	10/5/23	N/A	11/1/23	N/A	2/2/24	N/A	N/A	12/22/25									
Raw Development	2/16/24	2/24/2024																						
Jenks Fire Station	2/16/24	2/21/2024	3/4/24	7/10/24	2/29/24	2/29/24	2/29/24	N/A	N/A	7/9/24	3/12/25	1/8/25	10/16/25	9/22/25	12/18/25									
Burn Boot Camp (Fidler Acre)	6/13/23	8/20/2024	8/28/24	8/28/24	11/14/25	N/A	1/15/26	N/A	N/A	8/28/24	N/A	5/1/25	11/21/25	1/15/26										
Dollar General II (121st and Elm)	4/18/24	4/23/2024	1/14/25	1/20/25	6/10/24	6/10/24	6/10/24	2/12/25	2/12/25	2/7/25	5/15/25	5/15/25	5/15/25	5/15/25										
512 Gardens	2/9/23	N/A	7/11/23	7/18/23	N/A	N/A	7/11/23	N/A	N/A	7/18/23		12/23/25												
323 Gardens	2/9/23	N/A	8/24/23							1/24/25														
Stuco Apartments	1/24/24	4/19/2024	3/7/25	3/17/25	3/7/25	3/7/25	3/7/05	8/27/24	8/27/24	3/12/25	4/17/25													
Elwood Dental	10/28/24	N/A	2/26/25	3/3/25	N/A	N/A	2/26/25	N/A	N/A	2/21/25	N/A	N/A												
Bridgepoint (131st and Harvard)		12/5/2023	1/12/24	1/15/24	6/4/25	6/4/25	6/4/26	6/4/25	6/4/25	1/15/24														
Revitalize Medical Spa	8/5/24	N/A	10/24/24	10/28/24	N/A	N/A	10/24/24	N/A	11/14/24	10/28/24	1/10/25	7/14/25	7/14/25	7/14/25	N/A	N/A	8/7/25	8/19/25		6/19/26				
Chase Bank	10/1/24	4/10/2025	4/10/25	5/5/25	5/15/25	5/15/25	5/15/25	N/A	5/15/25	4/30/25	9/19/25	10/17/25	12/10/25	12/1/25	12/16/25									
High 5	1/17/23																							
Motorsports Collective	9/18/23	1/15/2025	1/15/25	1/20/25	1/15/25	N/A	1/15/25	N/A	N/A	2/25/25	N/A	11/14/25												
AAA "A" Street ("A" and 5th)	9/24/24	N/A	5/19/25	5/20/25	N/A	N/A	11/5/25	N/A	N/A	5/20/25	N/A	N/A												
Jenks Freshman Academy Phase III		3/16/2025	6/20/25	6/23/25	6/20/25	6/20/25	6/20/25	N/A	N/A	5/29/25														
Jazzercise	6/18/25	N/A	7/22/25	7/23/25	N/A	N/A	7/22/25	N/A	N/A	7/28/25	N/A	N/A												
Jenks Office Complex (East of S. Adams St. and South of Main St.)	8/13/25																							
Triple H Property (121 st St. and 27 th W. Ave)	12/5/24	7/25/2025	11/20/25	11/24/25	N/A	N/A	1/19/26	N/A		11/20/25														
First Baptist Jenks Parking Lot Expansion (116th St. and Elm St.)																								
W. K Pl. Office Buildings ("K" Pl. and Birch St.)	7/22/25																							
South County Crossing Lots 1 & 2	8/13/25	2/6/2026	1/5/26	1/20/26	5/26/26	N/A	5/26/26	N/A	N/A	1/5/26														
Far East Missions Church (129th St. and Harvard Ave.)	10/13/25																							
Jenks Bible Church (708 W. Main St.)	5/1/25	N/A			N/A	N/A	5/22/26	N/A	N/A	5/26/26														
Jenks Public Schools (JPS) Tennis Complex ("K" Pl. & Ash St.)	1/12/26																							
555 Aquarium Place Apartments (Aquarium Pl. & 5th St.)	6/9/25	N/A				N/A			N/A															

PROTECTIVE INSPECTIONS

MONTHLY REPORT

[illegible]

	Month of:	2026	City of Jenks Residential New Construction Application Log				April
#	Permit #	Date	Builder	Sub Division	Lot	Blk	Est. Const. Cost
1	RES-2026-0036	4/6/2026	Cozort Custom Homes	Pine Ridge	5	2	\$800,000.00
2	RES-2026-0037	4/6/2026	Cozort Custom Homes	Pine Ridge	7	3	\$700,000.00
3	RES-2026-0038	4/8/2026	Cozort Custom Homes	Harvard Oaks	5	3	\$300,000.00
4	RES-2026-0039	4/8/2026	Schuber Mitchell Homes	Frazier Meadows	6	9	\$215,820.00
5	RES-2026-0040	4/8/2026	Schuber Mitchell Homes	Frazier Meadows	8	10	\$283,360.00
6	RES-2026-0041	4/8/2026	Schuber Mitchell Homes	Frazier Meadows	5	9	\$217,400.00
7	RES-2026-0042	4/9/2026	Glenwood Homes	Harvard Oaks	4	5	\$365,515.00
8	RES-2026-0043	4/9/2026	Glenwood Homes	Harvard Oaks	1	5	\$326,360.00
9	RES-2026-0044	4/9/2026	Glenwood Homes	Harvard Oaks	3	1	\$336,797.00
10	RES-2026-0045	4/9/2026	Glenwood Homes	Harvard Oaks	3	4	\$385,919.00
11	RES-2026-0046	4/9/2026	Glenwood Homes	Harvard Oaks	1	4	\$326,360.00
12	RES-2026-0047	4/15/2026	Schuber Mitchell Homes	Frazier Meadows	7	10	\$288,680.00
13	RES-2026-0048	4/15/2026	Schuber Mitchell Homes	Frazier Meadows	11	11	\$326,040.00
13	RES-2026-0049	4/15/2026	J Davis Homes, LLC	Pine Ridge	3	4	\$579,320.00
14	RES-2026-0050	4/15/2026	J Davis Homes, LLC	Frazier Meadows	4	2	\$265,320.00
14	RES-2026-0051	4/20/2026	Schuber Mitchell Homes	Frazier Meadows	3	11	\$297,760.00
15	RES-2026-0052	4/20/2026	Schuber Mitchell Homes	Frazier Meadows	2	10	\$233,480.00
16	RES-2026-0053	4/20/2026	Schuber Mitchell Homes	Frazier Meadows	6	10	\$230,360.00
17	RES-2026-0054	4/24/2026	Crescent Homes Builders	Reserve at Southern Woods	12	6	\$586,040.00
18	RES-2026-0055	4/24/2026	Crescent Homes Builders	Harvard Oaks	11	6	\$570,880.00
19	RES-2026-0056	4/28/2026	Cozort Construction	Harvard Oaks	17	1	\$288,720.00
20							
21							
22							
23							
24							
25							
26							
27							
28							
29							
30							

City of Jenks
Commercial Permit Issued

April 2026

	Permit #	Builder	Sub Division	Projects	Est. Const. Cost	Issued Date	Total BP Fees
1	COM-2026-0018	Home Innovations	First Baptist Church	Office Space Remodel	\$25,000.00	4/30/26	\$559.00
2							
3							
4							
5							
6							
7							
8							
9							
10							
11							
12							
13							
14							
15							
16							
17							
18							
19							
20							
21							
22							
23							
24							
25							
26							
27							
28							
29							
30							
31							
32							
33							
34							
35							
36							
37							
38							
39							
40							
41							
42							
43							
44							
45							
46							
47							
48							
49							
50							
ESTIMATED CONSTRUCTION COST					BUILDING PERMIT FEES		
TOTAL: \$25,000.00					TOTAL: \$559.00		

Year End	City of Jenks	Commercial Construction	2026
Month:	Total: Permits	Estimated Construction Cost	Permit Fee's
January	2	\$190,000.00	\$ 1,961.00
Febuary	3	\$905,000.00	\$ 4,469.00
March	4	\$1,045,560.00	\$ 6,009.65
April	1	\$25,000.00	\$ 559.00
May			
June			
July			
August			
September			
October			
November			
December			
Total:	10	\$2,165,560.00	\$12,998.65

Year End	City of Jenks	Commercial Construction	2025-2026
Month:	Total Permits	Estimated Construction Cost	Permit Fee's
July	3	\$627,631.00	\$ 4,157.04
August	3	\$835,000.00	\$ 4,687.75
September	1	\$123,000.00	\$ 793.00
October	2	\$480,000.00	\$ 2,573.50
November	2	\$900,000.00	\$ 3,106.50
December	1	\$100,000.00	\$ 479.00
January	2	\$190,000.00	\$ 1,961.00
Febuary	3	\$908,000.00	\$ 4,469.00
March	3	\$875,000.00	\$ 4,675.25
April	1	\$25,000.00	\$ 559.00
May			
June			
Total:	21	\$5,063,631.00	\$ 27,461.04

City of Jenks
Residential New Home Permit Issued
April 2026

	Permit #	Builder	Sub Division	Lot	Blk	Est. Const. Cost	Issued Date	Total BP Fees
1	RES-2026-0032	Cozort Construction	Torrey Lakes	68	3	\$388,840.00	4/2/26	\$1,619.05
2	RES-2026-0024	Wilson Jackson Homes	Harvard Oaks	6	2	\$349,340.00	4/7/26	\$1,569.68
3	RES-2026-0022	Shane Cozort Homes	Harvard Oaks	9	2	\$318,760.00	4/8/26	\$1,531.45
4	RES-2026-0023	Shane Cozort Homes	Harvard Oaks	12	1	\$342,660.00	4/8/26	\$1,561.33
5	RES-2026-0030	BD Properties	Harvard Oaks	18	7	\$366,000.00	4/8/26	\$1,590.50
6	RES-2026-0045	Glenwood Homes	Harvard Oaks	3	5	\$325,040.00	4/10/26	\$1,539.30
7	RES-2026-0046	Glenwood Homes	Harvard Oaks	1	4	\$325,040.00	4/10/26	\$1,539.30
8	RES-2026-0042	Glenwood Homes	Harvard Oaks	4	5	\$321,020.00	4/10/26	\$1,534.28
9	RES-2026-0043	Glenwood Homes	Harvard Oaks	1	5	\$263,440.00	4/10/26	\$1,462.30
10	RES-2026-0044	Glenwood Homes	Harvard Oaks	3	1	\$268,240.00	4/10/26	\$1,468.30
11	RES-2026-0036	Cozort Custom Homes	Pine Ridge	5	2	\$479,100.00	4/15/26	\$1,731.88
12	RES-2026-0037	Cozort Custom Homes	Pine Ridge	7	3	\$407,060.00	4/15/26	\$1,641.83
13	RES-2026-0038	Cozort Custom Homes	Harvard Oaks	5	3	\$336,280.00	4/15/26	\$1,553.35
14	RES-2026-0035	Village Homes LLC	Pine Ridge	6	3	\$441,100.00	4/21/26	\$1,684.38
15	RES-2026-0039	Schuber Mitchell Homes	Frazier Meadows	6	9	\$230,360.00	4/28/26	\$1,370.95
16	RES-2026-0040	Schuber Mitchell Homes	Frazier Meadows	8	10	\$298,800.00	4/28/26	\$1,506.50
17	RES-2026-0041	Schuber Mitchell Homes	Frazier Meadows	5	9	\$246,900.00	4/28/26	\$1,391.63
18	RES-2026-0047	Schuber Mitchell Homes	Frazier Meadows	7	10	\$288,680.00	4/28/26	\$1,493.85
19	RES-2026-0048	Schuber Mitchell Homes	Frazier Meadows	11	11	\$326,040.00	4/28/26	\$1,540.55
20	RES-2026-0056	Cozort Construction	Harvard Oaks	17	1	\$288,720.00	4/29/26	\$1,493.90
21	RES-2026-0049	J Davis Homes	Pine Ridge	3	4	\$579,320.00	4/30/26	\$1,857.15
22								
23								
24								
25								
26								
27								
28								
29								
30								
31								
32								
33								
34								
35								
36								
37								
38								
39								
40								
41								
42								
43								
44								
45								
46								
47								
48								
49								
50								
ESTIMATED CONSTRUCTION COST						BUILDING PERMIT FEES		
TOTAL: \$7,190,740.00						TOTAL: \$32,681.46		

Year End	City of Jenks	Residential New Construction	2026
Month:	Total: Permits	Estimated Construction Cost	Permit Fee's
January	5	\$1,954,900.00	\$ 8,108.53
Febuary	9	\$3,406,280.00	\$ 14,404.86
March	7	\$2,715,860.00	\$ 10,975.83
April	21	\$7,190,740.00	\$ 32,681.46
May			
June			
July			
August			
September			
October			
November			
December			
Total:	42	\$15,267,780.00	\$66,170.68

Year End	City of Jenks	Residential New Construction	FY 2025-2026
Month:	Total Permits	Estimated Construction Cost	Permit Fee's
July	6	\$1,660,000.00	\$ 8,723.01
August	11	\$4,709,040.00	\$ 16,044.32
September	11	\$4,422,380.00	\$ 17,311.00
October	12	\$4,102,760.00	\$ 17,628.78
November	12	\$4,373,040.00	\$ 18,553.57
December	12	\$4,104,280.00	\$ 18,576.38
January	5	\$1,954,900.00	\$ 8,108.53
Febuary	9	\$3,406,280.00	\$ 14,404.86
March	7	\$2,715,860.00	\$ 10,975.83
April	21	\$7,190,740.00	\$ 32,681.46
May			
June			
Total:	106	\$38,639,280.00	\$ 163,007.74

City of Jenks
Misc Permit Issued

April 2026

	Permit #	Builder	Location/Project	Lot	Blk	Est. Const. Cost	Issued Date	Total BP Fees
1	SIGN-2026-0012	Souped Up Signs and Wraps	Motorsports Collective	12	1	\$14,000.00	10/20/00	\$294.00
2	RES-2026-0034	DLM Contractors	Southlake Villas	2	4	\$20,000.00	4/1/26	\$284.00
3	RES-2026-0033	Core Homes LLC	Clearfield Estates	12	3	\$48,500.00	4/2/26	\$384.75
4	POOL-2026-0012	Aquamarine Pools of Oklahma	Yorktown	3	31	\$25,000.00	4/6/26	\$284.00
5	POOL-2026-0014	Baker Pools LLC	Hickory Creek	7	6	\$60,000.00	4/7/26	\$409.00
6	POOL-2026-0028	Hertiage Pools	Dutchers Crossing	7	8	\$80,000.00	4/8/26	\$459.00
7	POOL-2026-0015	W Pool & Spas	Pecan Creek	8	2	\$80,000.00	4/9/26	\$459.00
8	POOL-2026-0016	Sierra Pools LLC	Country Woods	3	5	\$83,438.84	4/10/26	\$467.50
9	SIGN-2026-0013	Sign World of Tulsa	Extra Space Storage	1	1	\$2,500.00	4/17/26	\$284.00
10	SIGN-2026-0014	Sign World of Tulsa	Extra Space Storage	1	1	\$1,500.00	4/17/26	\$284.00
11	SIGN-2026-0015	Sign World of Tulsa	Extra Space Storage	1	1	\$1,500.00	4/17/26	\$284.00
12	6300	Dennis Vamer	Green Valley Estates	47	1	\$83,011.50	4/20/26	\$393.00
13	POOL-2026-0013	Tulsa Custom Pools	Gregory Circle Estates	3	3	\$55,000.00	4/20/26	\$321.50
14								
15								
16								
17								
18								
19								
20								
21								
22								
23								
24								
25								
26								
27								
28								
29								
30								
31								
32								
33								
34								
35								
36								
37								
38								
39								
40								
41								
42								
43								
44								
45								
46								
47								
48								
49								
50								
ESTIMATED CONSTRUCTION COST						BUILDING PERMIT FEES		
TOTAL: \$554,450.34						TOTAL: \$4,607.75		

Year End	City of Jenks	Misc. Construction	2026
Month:	Total: Permits	Estimated Construction Cost	Permit Fee's
January	6	\$402,700.00	\$ 2,152.50
Febuary	9	\$502,489.72	\$ 3,155.48
March	13	\$402,312.50	\$ 3,577.03
April	4	\$1,045,560.00	\$ 6,009.65
May	13	\$554,450.34	\$ 4,607.75
June			
July			
August			
September			
October			
November			
December			
Total:	45	\$2,907,512.56	\$19,502.41

Year End	City of Jenks	Misc. Construction	FY 2025-2026
Month:	Total Permits	Estimated Construction Cost	Permit Fee's
July	9	\$340,088.43	\$ 2,861.50
August	20	\$571,317.97	\$ 5,450.93
September	16	\$1,116,232.09	\$ 6,173.22
October	6	\$329,099.00	\$ 2,322.76
November	8	\$247,598.43	\$ 2,245.25
December	12	\$658,382.40	\$ 3,838.50
January	6	\$402,700.00	\$ 2,152.50
Febuary	9	\$502,489.72	\$ 3,155.48
March	13	\$402,312.50	\$ 3,577.03
April	13	\$554,450.34	\$ 4,607.75
May			
June			
Total:	112	\$5,124,670.88	\$ 36,384.92
